Project Scope

A web platform designed to connect students (Skill Seekers) with tutors (Skill Providers) in Syria. The platform enables students to find tutors based on skills and availability, book sessions, and leave reviews. Tutors can set their availability, manage bookings, and receive feedback to build their professional reputation.

Module	Description	Status
User Mgmt.	Register skill seekers and providers	**In Scope**
Skills Mgmt.	Search, add, categorize and upload qualifications	**In Scope**
Scheduling	Availability calendar for skill providers, request, confirm or reject and notify	**In Scope**
AI search and recommendations	Skill providers suggestions based on skills, urgency and ratings	**In Scope**
Review System	Rating and feedback (optional)	**In Scope**
Payment	Online payment via card numbers and bank transfers	**Out of Scope**
Online sessions	Live Video/Audio chats	**Out of Scope**
Sessions upload	Prerecorded sessions, meetings and lectures	**Out of Scope**
Mobile App	Native iOS, Android application	**Out of Scope**

Methodology

Hybrid:

Waterfall for planning: to have a complete and fixed plan.
Agile for building: for better flexibility.

Why not just waterfall?

No feedback until the end.
Unable to change.

Why not just agile?

No overall plan.
Inconsistent.
Endless changes.

GANTT CHART

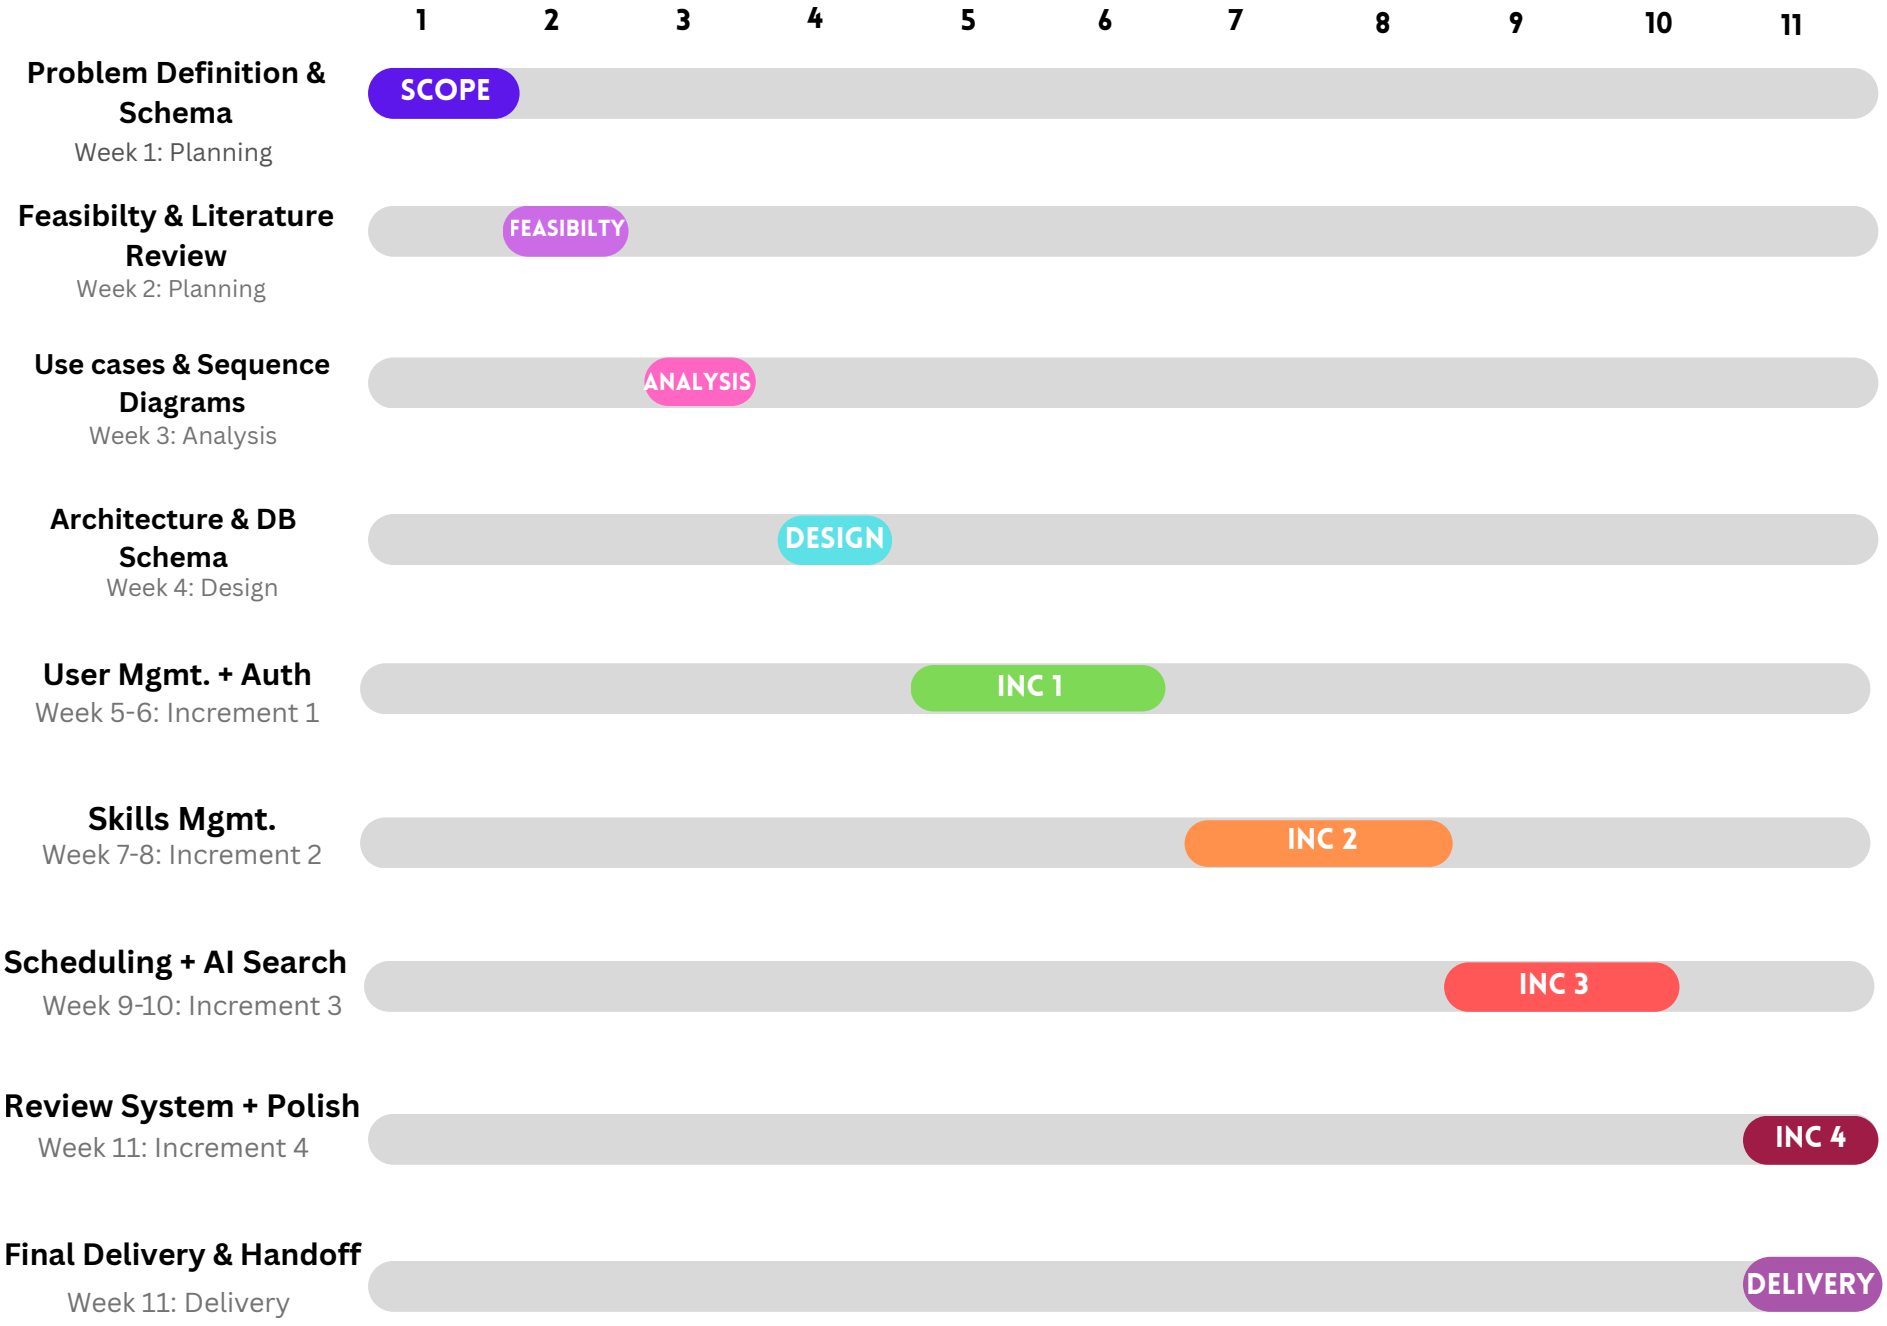
1
2
3
4
5
6
7
8
9
10
11
Problem Definition & Schema
Week 1: Planning
SCOPE
Feasibilty & Literature Review
Week 2: Planning
FEASIBILTY
Use cases & Sequence Diagrams
Week 3: Analysis
ANALYSIS
Architecture & DB Schema
Week 4: Design
DESIGN
User Mgmt. + Auth
Week 5-6: Increment 1
INC 1
Skills Mgmt.
Week 7-8: Increment 2
INC 2
Scheduling + AI Search
Week 9-10: Increment 3
INC 3
Review System + Polish
Week 11: Increment 4
INC 4
Final Delivery & Handoff
Week 11: Delivery
DELIVERY

Project Charter

Project Title: YT²uTor

Project Start Date: March 10, 2026

Project Finish Date: May 23, 2026

Project Manager: Dr. Anas Abdulaziz

Project Objectives:

Develop a web platform to connect students with verified tutors in Syria by providing real-time availablity tracking, booking management, and a reputation-based review.

Approach:

1. Define project scope and objectives.
2. Analyze system requirements and specifications.
3. Design system architecture and database schema.
4. Develop the first increment, focusing on *User Management and Authentication.*
5. Develop the second increment, focusing on *Skills Management and qualification uploads.*
6. Develop the third increment, focusing on the *Scheduling system and semantic search recommendations.*
7. Implement the Review System and perform final UI refinements.
8. Document all development phases and outcomes for final submission.

Roles and Responsibilities:	**Name**	**Responsibility**
Dr. Anas Abdulaziz	Project Manager / Supervisor	Project management oversight and work monitoring
Eng. Mohamed al Balkhi	Supervisor	Technical guidance and work monitoring
Yara Jabr	Engineer	Backend development
Tebella Danho	Engineer	Frontend development
Tasnim Murai	Engineer	Frontend development

Risk Overview

Risk Category	Risk Description	Risk Level	Solution
Technical	System performance degradation with many users	Medium	Improve database queries, add indexes, use caching, show fewer results per page
Security	Protecting user data	High	Use HTTPS and keep files in a secure place with access controls
Legal/Safety	Possible misuse after tutor-student connection	Low	Add safety rules, add a report button, encourage meeting in public places, include a disclaimer
Schedule	Very short 10-week timeline	High	Focus on core features first, use short sprints, deliver small working pieces
Human Resources	Team still learning while building	High	Use AI tools for help, pair up while working, focus on understanding
Market/Technical	Slow internet in Syria	Medium	Keep pages light, keep files small, make sure basic use works even on slow internet
Market/Trust	Gaining user trust	Medium	Use ratings and reviews, show verification status, show session history and clear profiles
